

Sydney Swans Headquarters & Community Centre



Progress Photo Report 16

DATE: 17/12/2021

Project Number: 100390

Address: Royal Hall of Industries, 1 Driver Avenue, Moore
Park NSW

Site Walk (17/12/21)

Description

Lift core formwork
stripped and waterproofed

Taken Date

17/12/2021 at 09:42 am

Upload Date

17/12/2021 at 10:17 am

Uploaded By

Dylan Luisi

File Name

[A2E7B016-D961-46AF-B...](#)



Site Walk (17/12/21)

Description

Basement excavation for
new extension

Taken Date

17/12/2021 at 09:40 am

Upload Date


17/12/2021 at 10:18 am

Uploaded By

Dylan Luisi

File Name

[0F4F0E91-2745-4A7D-9...](#)

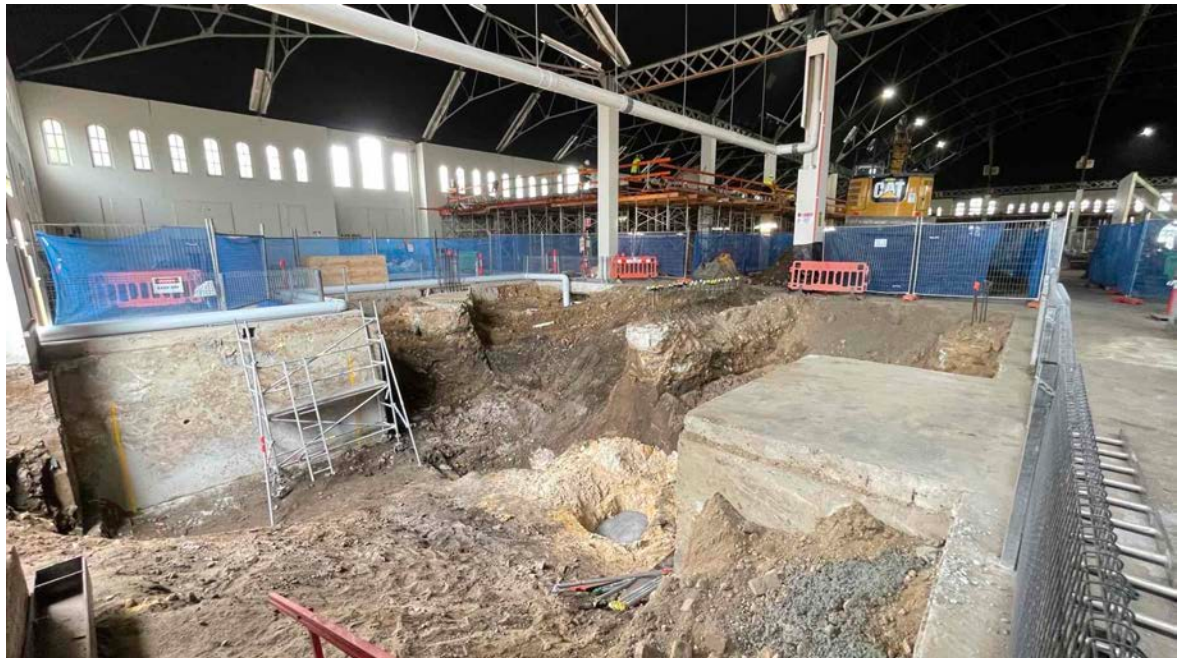

Site Walk (17/12/21)

Description
Pour B concrete finish

Taken Date
17/12/2021 at 09:36 am

Upload Date
17/12/2021 at 10:18 am

Uploaded By
Dylan Luisi

File Name
[01DD90C0-674F-4BC0-8...](#)



Site Walk (17/12/21)


Description
Pour B concrete pour

Taken Date
17/12/2021 at 09:35 am

Upload Date
17/12/2021 at 10:18 am

Uploaded By
Dylan Luisi

File Name
[CBB5E61E-8C07-4EA1-A...](#)

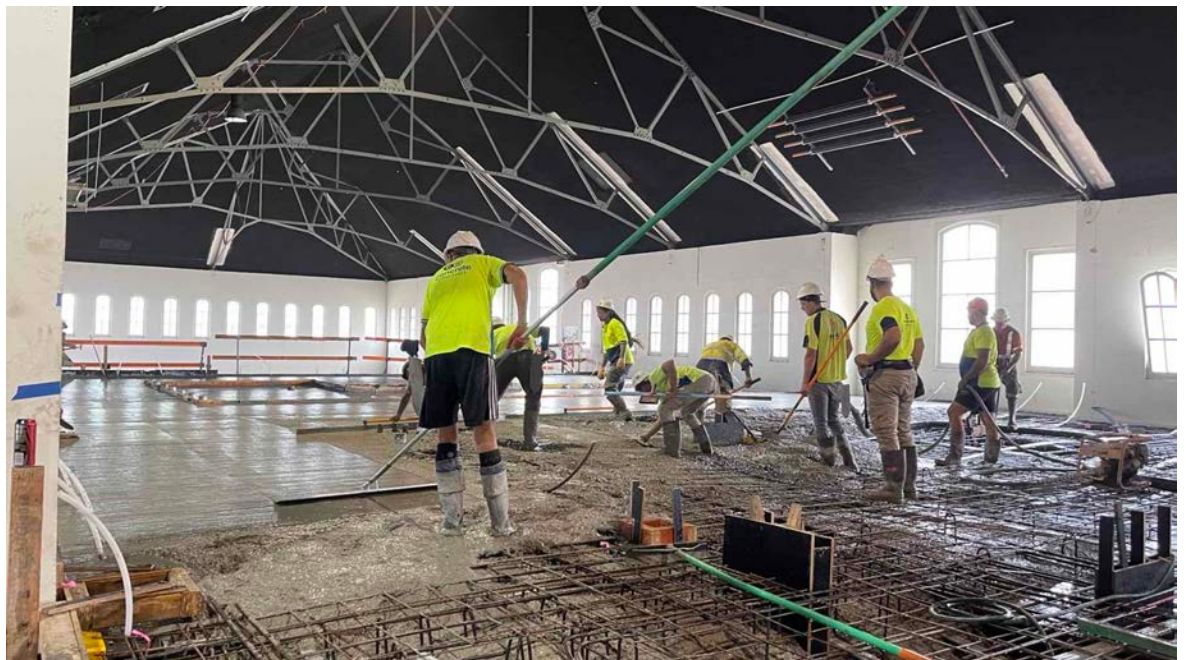

Site Walk (17/12/21)

Description

Pour B concrete boom pump providing clear access for the concrete pour

Taken Date

17/12/2021 at 09:34 am

Upload Date

17/12/2021 at 10:18 am

Uploaded By

Dylan Luisi

File Name

8D64DBB1-FB8E-441F-9...



Site Walk (17/12/21)

Description

Pour A reinforcement installation to tie into the lift shaft and services rough in

Taken Date

17/12/2021 at 09:33 am

Upload Date


17/12/2021 at 10:18 am

Uploaded By

Dylan Luisi

File Name

6FA99076-34A5-4DA7-B...

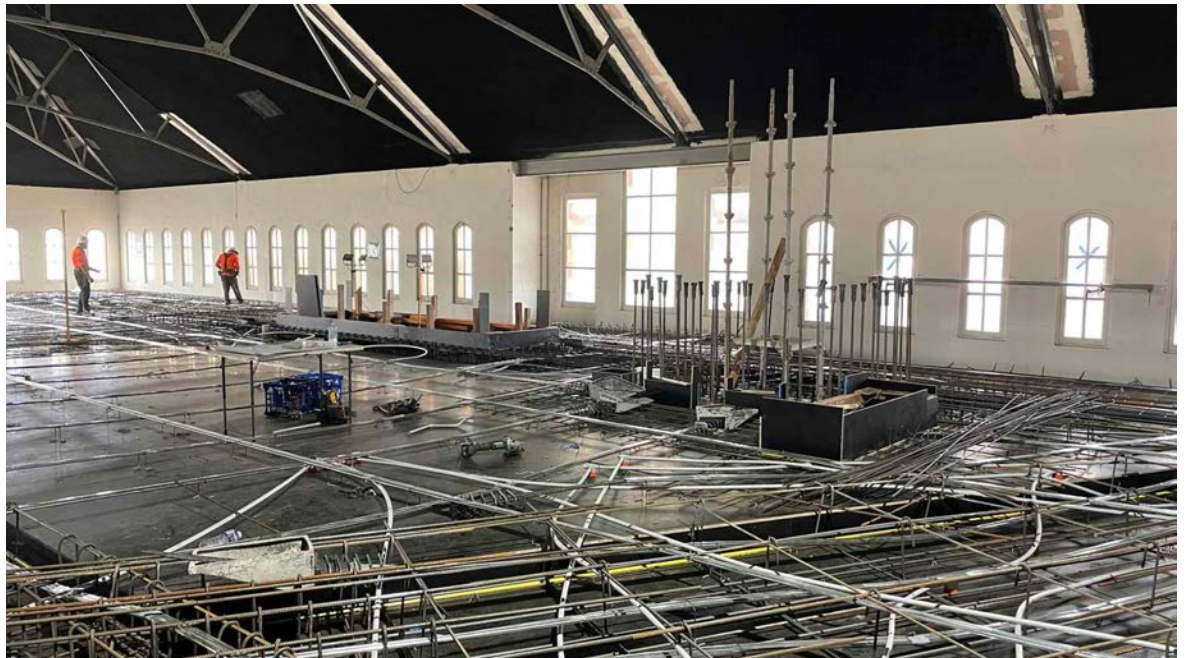

Site Walk (17/12/21)

Description
Pour B concrete pour

Taken Date
17/12/2021 at 09:32 am

Upload Date
17/12/2021 at 10:18 am

Uploaded By
Dylan Luisi

File Name
[1A14DB08-7DFA-4AF5-A...](#)



Site Walk (17/12/21)

Description
Pour B concrete pour

Taken Date
17/12/2021 at 07:19 am

Upload Date
17/12/2021 at 12:11 pm

Uploaded By
Dylan Luisi

File Name
[fdcskansint_20211217_...](#)



Site Walk (17/12/21)

Description
Pour B concrete pour

Taken Date
17/12/2021 at 07:04 am

Upload Date
17/12/2021 at 12:11 pm

Uploaded By
Dylan Luisi

File Name
[fdcskansint_20211217_...](#)



Site Walk (17/12/21)

Description
Lift core concrete pour

Taken Date
16/12/2021 at 05:19 pm

Upload Date
17/12/2021 at 10:18 am

Uploaded By
Dylan Luisi

File Name
[FD708910-8519-483C-9...](#)



Site Walk (17/12/21)

Description

Lift core concrete pour

Taken Date

16/12/2021 at 05:00 pm

Upload Date

17/12/2021 at 12:10 pm

Uploaded By

Dylan Luisi

File Name

[fdcswansext_20211216_...](#)



Site Walk (17/12/21)

Description

Remaining piles following
Ausgrid disconnect

Taken Date

16/12/2021 at 10:30 am

Upload Date

17/12/2021 at 12:10 pm

Uploaded By

Dylan Luisi

File Name

[fdcswansext_20211216_...](#)



Site Walk (17/12/21)

Description

Basement excavation soil removal, pour B prepared for inspection prior to concrete pour

Taken Date

15/12/2021 at 01:19 pm

Upload Date

17/12/2021 at 12:10 pm

Uploaded By

Dylan Luisi

File Name

[fdcskansint_20211215_...](#)



Site Walk (17/12/21)

Description

Crane lift to remove remaining redundant AHUs

Taken Date

14/12/2021 at 10:00 am

Upload Date

17/12/2021 at 12:08 pm

Uploaded By

Dylan Luisi

File Name

[fdcskansext_20211214_...](#)



Site Walk (17/12/21)

Description
Basement excavation and
pour C formwork
installation

Taken Date
13/12/2021 at 03:19 pm

Upload Date
17/12/2021 at 12:10 pm

Uploaded By
Dylan Luisi

File Name
[fdcswnsint_20211213_...](#)



Site Walk (17/12/21)

Description
Sewer inground
connection works

Taken Date
13/12/2021 at 11:30 am

Upload Date
17/12/2021 at 12:08 pm

Uploaded By
Dylan Luisi

File Name
[fdcswnsxt_20211213_...](#)

